
EOSC | GRAVITY

Cascading grant project: Preparatory

Project acronym: EOSC-ES-Prep

Project deliverable: Project plan

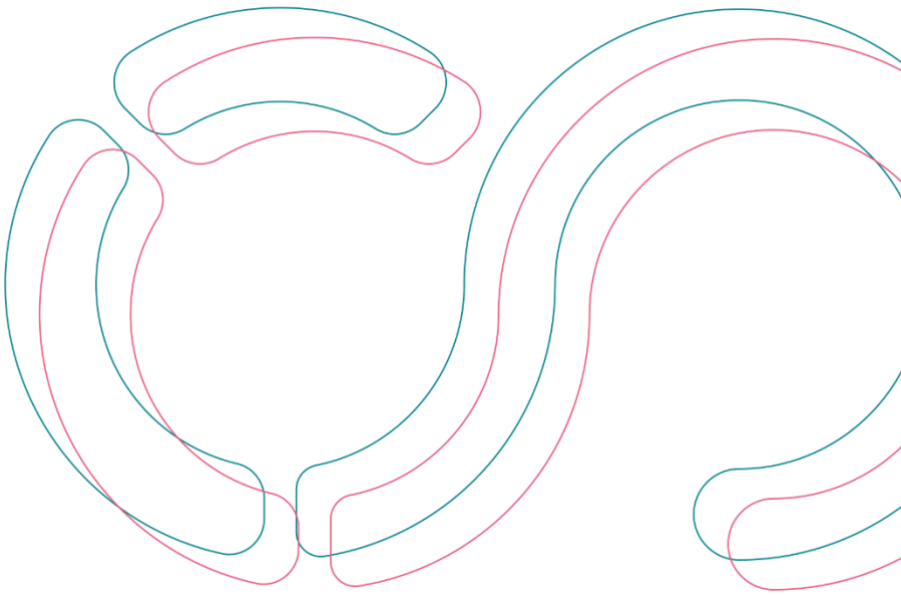

Funded by
the European Union

Cascading project name and acronym	EOSC-ES-Prep
Grant ID of the cascading project	EOSCGRAVITY-PREP-2026-010-EOSC-ES-PREP
Lead beneficiary	IACS (Instituto Aragonés de Ciencias de la Salud)
Authors	Juan González-García (IACS), Ignacio Blanquer-Espert (UPV), Daniel Garijo (UPM), Helena Lozano (CSIC), on behalf of the EOSC-ES-Prep consortium
Due date	M2 – June 6
Approved on	

Disclaimer

This project has been funded within the Cascading Grants under the EOSC Gravity Project, which has received funding from the European Union's Horizon Europe programme under Grant Agreement No. 101188045.

The views and opinions expressed herein are those of the author(s) only and do not necessarily reflect those of the European Union, the granting authority and the EOSC Gravity partners. Neither the European Union, nor the granting authority or EOSC Gravity partners can be held responsible for them.

The deliverables are assessed solely in accordance with the formal criteria of the call. The review process seeks to maintain an impartial and unbiased position and to avoid any conflict of interest. It does not include the evaluation or endorsement of the technical or operational solutions proposed by the grantees. Consequently, the reviewers cannot be held responsible for any inaccuracies, shortcomings, or errors that may appear in the submitted materials or related project documentation.

Copyright notice

Except where otherwise stated, this work is licensed under CC BY 4.0.

Table of Contents

1 PROJECT SUMMARY 3
2 ACTION PLAN 3
3 KEY PERFORMANCE INDICATORS (KPIS) 4
4 RISK ASSESSMENT **5**

Funded by the European Union
Grant agreement ID: 101188045

1 Project summary

Project summary
EOSC-ES-Prep prepares the future Spanish EOSC Node (EOSC-ES) for enrolment into the EOSC Federation. The project translates Spain's open-science policy commitments in relation to EOSC into an operational, governance-ready node proposal aligned with the EOSC Federation Handbook and Memorandum of Understanding. It will (i) inventory and map Spanish e-infrastructures, ICTS, data spaces, repositories and open-science services against federation requirements; (ii) propose a sustainable governance model for a distributed national ecosystem; and (iii) specify an initial service portfolio, federating capabilities and interaction mechanisms with other EOSC Nodes and the EOSC Academy. The project responds to the current fragmentation of EOSC-related activities in Spain by proposing a coordinated national umbrella that improves visibility, access and reuse of research data, software and services. It draws on a strong consortium of 22 Spanish institutions, including national research infrastructures, universities, biomedical institutes and e-infrastructure operators, with expertise in AAI, HPC, FAIR data, repositories, training, semantic services and community engagement. Alignment with the emerging Data Spaces will also be considered. Expected benefits include improved national coordination, a clear onboarding pathway to the EOSC Federation, validated cross-disciplinary use cases, and reusable training and engagement materials that strengthen Spain's long-term participation in EOSC. Key outputs are: D1 Project Plan (M1), D2 EOSC-ES Project Charter (M4), D3 Draft Plan for a Showcase Event (M4), D4 Short Use Case Report (M6), D5 Showcase Event Contribution (M6) and D6 EOSC Academy Contribution Matrix (M6).

2 Action plan

N	Date	Objective	Activity
1	May 2026	Operational baseline and governance launched	Kick-off the project, confirm roles and work stream ownership, establish coordination mechanisms, create the risk register, and deliver D1 Project Plan.
2	June 2026	Charter scope and governance boundaries agreed	Hold the first face-to-face workshop to validate the value proposition, governance model, EOSC Federation requirements, and criteria for selecting repositories and use cases. Alignment and interoperability with the emerging Data Spaces will also be considered.

N	Date	Objective	Activity
			Continuous communication to participate on EOSC Academy courses.
3	July 2026	Core deliverables drafted	Draft the EOSC-ES Project Charter and initial use case report. Online meeting to consolidate inputs from first deliverable Prepare the structure and key messages for showcase and dissemination contributions.
4	August 2026	First complete outputs finalised	First half: draft D2 EOSC-ES Project Charter and D3 Draft Plan for a Showcase Event, during first half. Second half: Circulate documents across consortium for validation and final consolidation. Start the EOSC Academy Contribution Matrix.
5	September 2026	Tripartite alignment and validation completed	Second face-to-face event alongside with the EOSC Spain Tripartite, to discuss and validate the integrated project narrative towards final project charter submission. Additionally, select the exemplar use case to create the D4 Short Use Case Report and start the drafting of the D5 Showcase Event Contribution, and D6 EOSC Academy Contribution Matrix
6	October 2026	Final readiness package delivered	During the first half, finish the drafting of D4 Short Use Case Report, D5 Showcase Event Contribution, and D6 EOSC Academy Contribution Matrix. During the second half, circulate the deliverables across the consortium and consolidate the results for its submission. Final online meeting to assess the EOSC-ES readiness for EOSC Federation and align next steps.

3 Key Performance Indicators (KPIs)

N	KPI Description	Target	Reached by
1	Participating institutions and key national assets mapped against EOSC requirements	10 co-applicant institutions and relevant national assets mapped	M2
2	Governance model and node scope defined	Proposal governance model and charter structure agreed among co-applicants	M2
3	Mandatory Federating Capabilities planning completed	Pathways for 5 mandatory capabilities documented (AAI, catalogue, helpdesk, monitoring, service management)	M4
4	Project Charter completed and internally validated	D2 submitted	M4
5	Archetypical use cases analysed and prioritised	2 intra-node use cases analysed, and 1 inter-node cross-disciplinary analysed	M6
6	Community engagement actions delivered	2 face-to-face events and 2 online meetings completed	M6
7	Training contribution prepared for EOSC Academy	10 co-applicants participate and evaluate EOSC Academy contents	M6
8	Overall project delivery completed	6/6 planned deliverables submitted	M6
9	Alignment actions with European and national data space interoperability frameworks	At least 3 strategic alignment actions related to the Data Spaces, such as SIMPL, UNE 0087:2025 data space characterisation principles, or EHDS-EOSC coordination.	M6

4 Risk assessment

N	Description	Severity (high-medium-low)	Probability (high-medium-low)	Mitigation measures
1	Limited availability or drop-off of volunteer contributors	High	Medium	Confirm commitments early, assign clear time-bounded tasks, and broaden participation through existing EOSC-ES collaboration channels. Frequent monitoring of progress.
2	Insufficient political or institutional support	High	Medium	Maintain alignment with national Open Science initiatives, organise stakeholder briefings, and

N	Description	Severity (high-medium-low)	Probability (high-medium-low)	Mitigation measures
				communicate a clear value proposition.
3	Rapid evolution of EOSC policies or technical guidelines	Medium	High	Continuously monitor EOSC Federation Handbook and Tripartite updates, and keep revision checkpoints in the workplan.
4	Coordination overhead from distributed voluntary governance	Medium	Medium	Use a simple governance structure, focused meetings, lightweight reporting, and written decision records.
5	Misalignment with minimum EOSC Node requirements	High	Low	Perform early self-assessment and peer review of governance, technical readiness, and community engagement requirements. Involve key actors from other nodes.
6	New partners hesitate to engage because of perceived duplication with other data spaces	High	Low-Medium	Position EOSC-ES as a value-added interoperability layer for discovery and reuse, and identify complementarity pathways and resources (such those from e-Infrastructures and Research Infrastructures) with existing data spaces.
7	Divergence between EOSC onboarding activities and evolving European data space interoperability frameworks	Medium	Medium	Monitor developments related to European and national data spaces governance frameworks and selected technologies, ensuring continuous coordination with relevant national and European initiatives.
